



FACILITIES MANAGEMENT  
Capital Construction & Renovation

Date: June 1, 2020

Report No. **10**

CONSTRUCTION PROJECT STATUS REPORT  
**Student Health & Wellness Center**

**Construction Manager:**

Barton Malow Company, Charlottesville, VA

**Architects:**

VMDO & Duda Paine

**Current Status:**


Construction Start: March 5, 2019  
Construction Completion: March 31, 2021 Substantial Completion  
**Completion Status:** 48% Complete Bid Package

**Current Activities**

Site Utilities  
CMU Masonry  
Cold Form Metal Stud Framing  
Sheathing  
Mechanical Piping & Ductwork  
Electrical, Plumbing  
Fireproofing, Fire Protection  
Roofing

**Future Activities:**

Mechanical, Electrical  
Equipment Exterior Sheathing  
Waterproofing

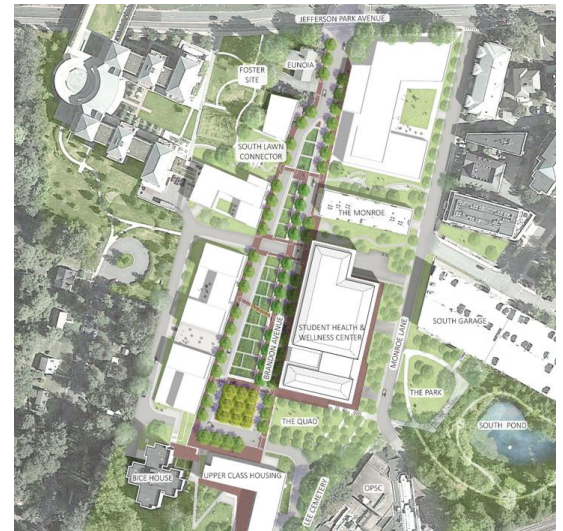

Report prepared by:  
Amy Eichenberger, UVA Senior Project Manager  
[ace8a@virginia.edu](mailto:ace8a@virginia.edu)  
(434) 924-8627

Richard Sergi is the UVA Senior Construction Administration Manager  
[rfv4v@eservices.virginia.edu](mailto:rfv4v@eservices.virginia.edu)  
(434) 996-4570



**Recent Construction Photos:**





















