



FACILITIES MANAGEMENT
Capital Construction & Renovation

Date: July 22, 2021

Report No. 17

CONSTRUCTION PROJECT STATUS REPORT
Student Health & Wellness Center

Construction Manager:

Barton Malow Company, Charlottesville, VA

Architects:

VMDO & Duda Paine

Current Status:

Construction Start:

March 5, 2019

Construction Completion:

August 23, 2021 Substantial Completion

Completion Status: 96%

Complete Bid Package

Current Activities

Interior Painting & Finishes

Millwork

Furniture and Equipment

Mechanical, Electrical, Plumbing

Life Safety Systems Testing

Landscape Final Grading and Prep

Future Activities:


Interior Painting & Finishes

Mechanical, Electrical, Plumbing

Life Safety Systems Testing

Mechanical Systems Test and Balance

Landscaping

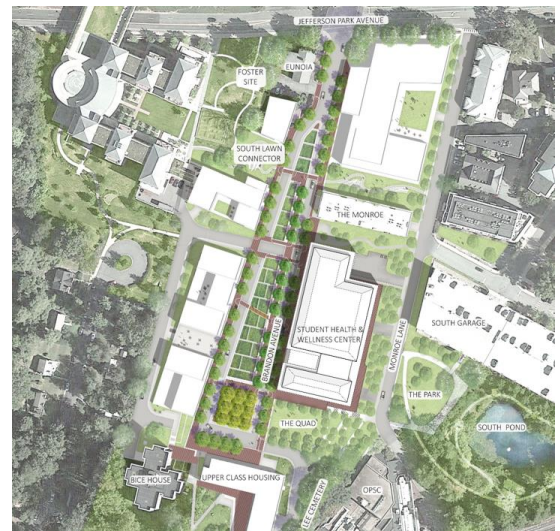

Report prepared by:

Amy Eichenberger, UVA Senior Project Manager

ace8a@virginia.edu

(434) 924-8627

Richard Sergi is the UVA Senior Construction Administration Manager

rfs4v@eservices.virginia.edu

(434) 996-4570

Recent Construction Photos:



