



FACILITIES MANAGEMENT
Facilities Planning and Construction Department

DATE: Nov. 28, 2016

CONSTRUCTION ALERT UPDATE

Report No. 13

CONCERNING IMMINENT CONSTRUCTION ACTIVITY

35kV Ductbank Project

ITEMS OF INTEREST: Construction activity will begin in front of the Alderman Substation in the FM Shop area on Tuesday, Nov. 29 ~~Monday, Dec. 5~~. Construction will start in front of the Alderman Substation and move towards Alderman Road. Faulconer will be working in small sections to ensure that there is access to the parking areas and substation.


IMMINENT ACTIVITY: There will be construction activity in the FM parking area starting in late Nov. and ending in early January 2017.

BACKGROUND: The 35kV Ductbank Project will install 2.75 miles of 35 kV electrical ductbank to provide a dedicated underground power feed to the University of Virginia. The new ductbank will connect the existing Sherwood, Alderman, and Cavalier substations through a combination of two, four, and six way underground ductbanks consisting of 8" PVC conduits encased in concrete. Large concrete electrical vaults will be installed at approximately 500 foot intervals along the ductbank, the largest vaults measure 9'x9'x17' outside dimensions. The installation of the ductbank requires road closures in several areas.

INTERIM ROUTES: Alternate routes will be established when necessary.

ISSUED BY: Dave Fiero, Project Manager/Senior Construction Administration Manager, FP&C, DFiero@virginia.edu, 434-297-7630, c 434.872-1469

Caitlin Murtaugh, Project Coordinator, FP&C, cm8nf@virginia.edu, 434.982.2956, c 434.906.3075

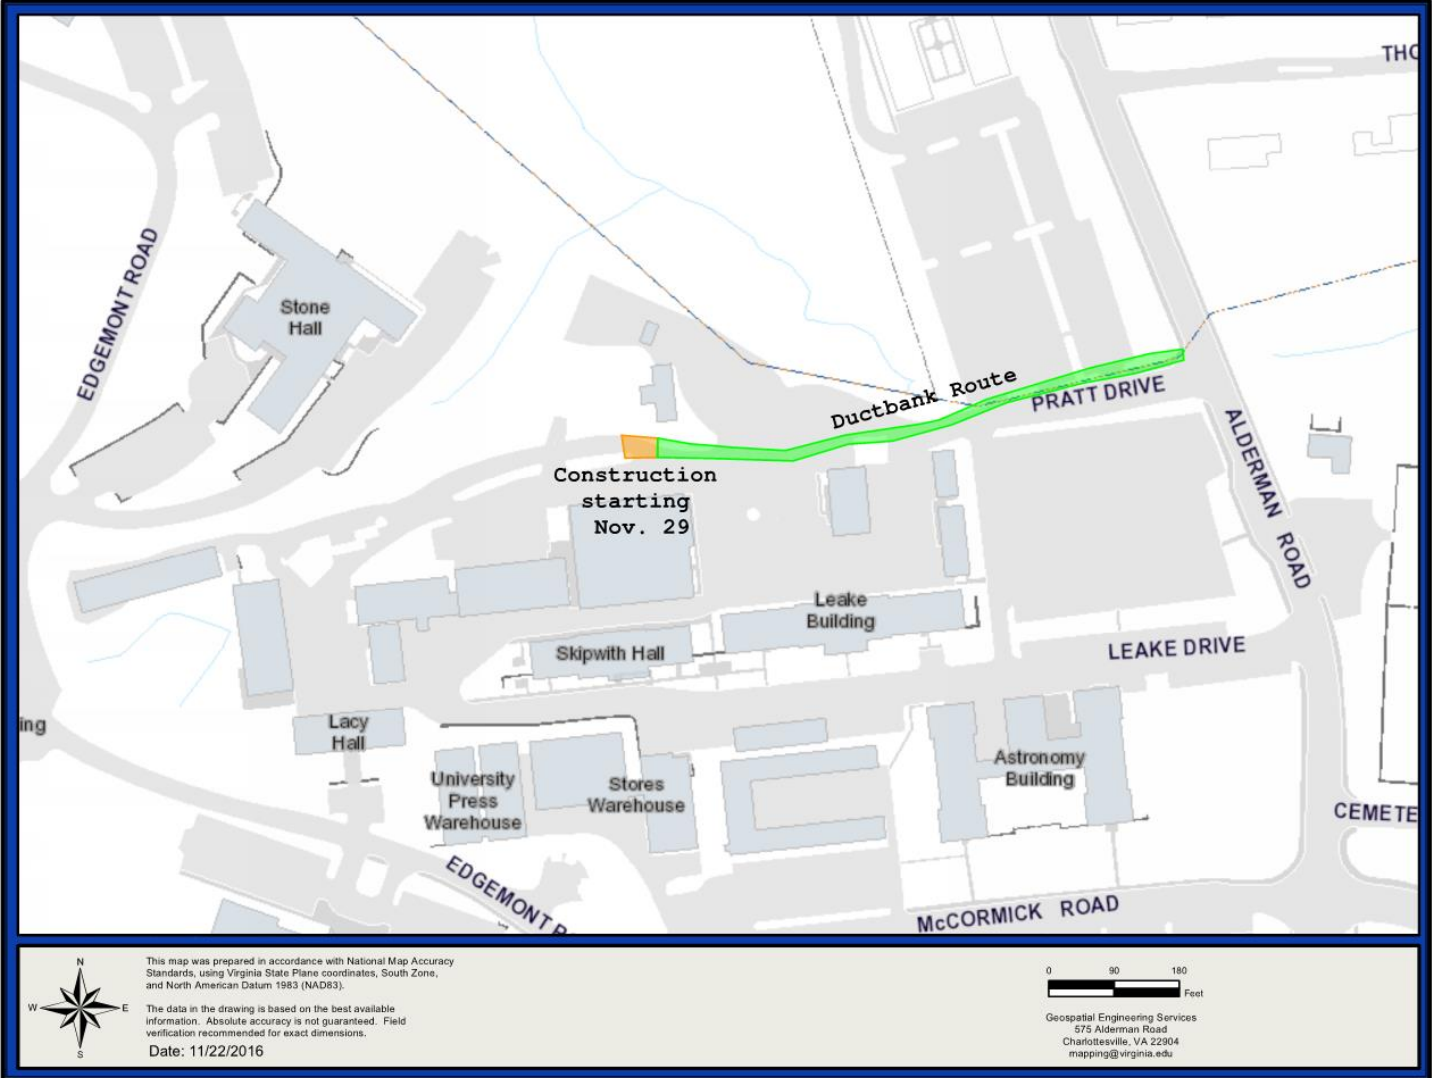

END OF ALERT
