



FACILITIES MANAGEMENT  
Facilities Planning and Construction Department

DATE: April 27, 2017

## **CONSTRUCTION ALERT**

Report No. 30

### **CONCERNING IMMINENT CONSTRUCTION ACTIVITY**

## **35kV Ductbank Project Update**


**ITEMS OF INTEREST:** Construction activity will be starting in the Stadium/Emmet Island from May 1, 2017 to May 8, 2017. Faulconer Construction will be installing an underground electrical vault.

**BACKGROUND:** The 35kV Ductbank Project will install 2.75 miles of 35 kV electrical ductbank to provide a dedicated underground power feed to the University of Virginia. The new ductbank will connect the existing Sherwood, Alderman, and Cavalier substations through a combination of two, four, and six way underground ductbanks consisting of 8" PVC conduits encased in concrete. Large concrete electrical vaults will be installed at approximately 500 foot intervals along the ductbank, the largest vaults measure 9'x9'x17' outside dimensions. The installation of the ductbank requires road closures in several areas.

**INTERIM ROUTES:** There will be temporary routes in place for pedestrian traffic. There will be no changes to vehicular traffic.

**ISSUED BY:** Dave Fiero, Project Manager/Senior Construction Administration Manager, FP&C, [DFiero@virginia.edu](mailto:DFiero@virginia.edu), 434-297-7630, c 434.872-1469

Caitlin Murtaugh, Project Coordinator, FP&C, [cm8nf@virginia.edu](mailto:cm8nf@virginia.edu), 434.982.2956, c 434.906.3075

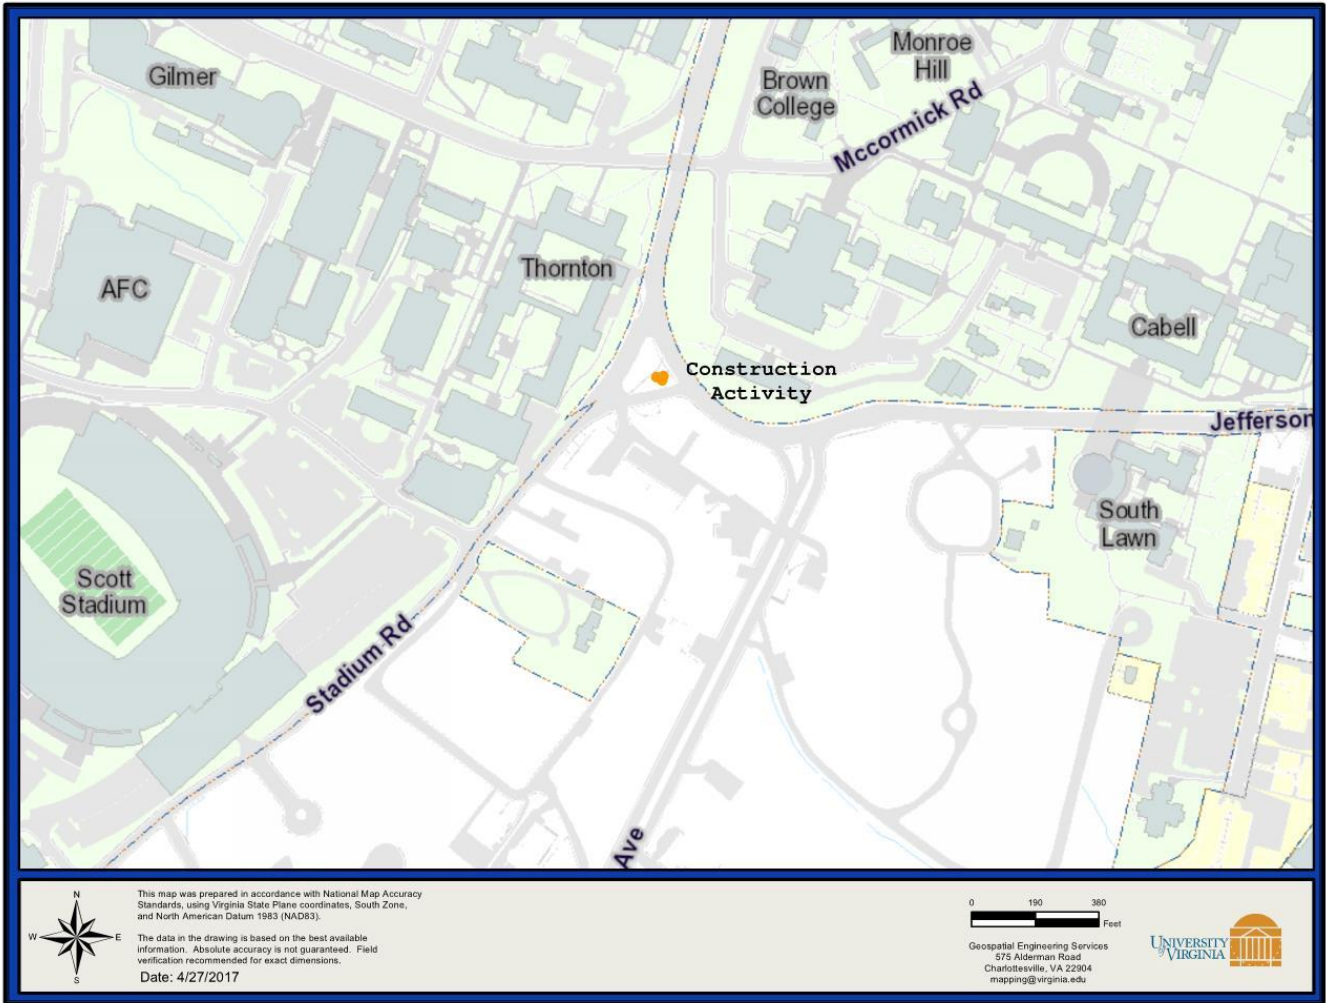

END OF ALERT
